

Work Order ID 134422

Wednesday, July 08, 2015 3:13:43 PM

134422

Page 1

Item ID: D6101-015 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Saddle Billet
Start Date: 7/06/15 Start Qty: 20.00 ***20*** Cust Item ID:
Required Date: 7/07/15 Req'd Qty: 20.00 ***20*** Customer:
Reference:

Approvals: Process Plan: MLS Date: JUL 09 2015 Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____
Run Start ***NR1***
Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr								
D6101	B								

100 PURCHASING 0.00 CL 15/07/10 20

100

Purchasing

Memo

0.00

Purchasing

Issue P/O: 29100

a) Description: Aluminum billet

b) 9.450" x 6.250" x 2.50" thick (+0.030 / -0.000)

c) Tolerance on all dimensions are +0.030/-0.000"

d) Grain direction along 9.450" length

e) Material: 7075-T7351 (QQ-A-250/12)

f) Material certification required

110 Receive & Inspect for Damage & Mat'l Certs 0.00 20x 8015-07-28

110

Packaging

Memo

0.00

Packaging

Ensure material certification is attached

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐	OTHER : _____			

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐				FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐					
OTHER : ☐									

Picklist Print

Wednesday, July 08, 2015 3:13:43 PM

Page 1

Work Order ID: 134422

134422

Parent Item: D6101-015

D6101-015

Parent Item Name: Saddle Billet

Start Date: 7/06/15

Required Date: 7/07/15

Start Qty: 20.00

Required Qty: 20.00

Comments: IPP RevA: New issue DD verified by:EC

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D6101-015P		Purchased	No			110	Each	0.0000	1	20			

D6101-015P

ALUM BILLET

20x SPIS 07-28

DQA: _____ Date: _____




WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation			Disposition		
			Completed By		
			Lead hand / Supervisor Approval Verification		
			QC / QA Coordinator Approval		
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : _____					

SPECIFICATION CONTROL DRAWING

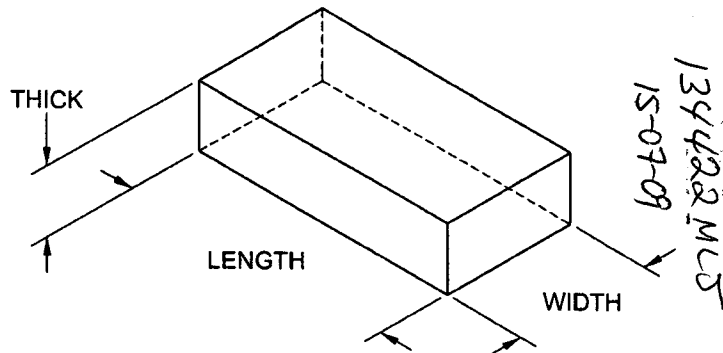

PURCHASE MATERIAL ACCORDING TO THE FOLLOWING TABLE. SPECIFY ALLOY, LENGTH x WIDTH x THICK (+0.030/-0.000), AND GRAIN DIRECTION AS SHOWN.

TOLERANCES ON ALL DIMENSIONS ARE +0.030/-0.000.

ALL DIMENSIONS ARE IN INCHES.

B ACCEPTABLE SPECIFICATIONS FOR 7075-T7351 ALUMINUM ARE AMS-QQ-A-250/12, QQ-A-250/12, OR ASTM B209

Part No.	Alloy	Length	Width	Thick	Grain Direction
D6101-001	7075-T7351 (QQ-A-250/12)	6.000	6.250	2.000	Along 6.000 Length
D6101-003	7075-T7351 (QQ-A-250/12)	7.875	6.250	2.000	Along 7.875 Length
D6101-005	7075-T7351 (QQ-A-250/12)	5.000	8.250	2.500	Along 5.000 Length
D6101-007	7075-T7351 (QQ-A-250/12)	7.750	8.250	2.500	Along 7.750 Length
D6101-009	7075-T7351 (QQ-A-250/12)	8.700	8.250	2.500	Along 8.700 Length
D6101-011	7075-T7351 (QQ-A-250/12)	9.700	8.250	2.500	Along 9.700 Length
D6101-013	7075-T7351 (QQ-A-250/12)	10.100	8.250	2.500	Along 10.10 Length
B D6101-015	7075-T7351 (QQ-A-250/12)	9.450	6.250	2.500	Along 9.450 Length
D6101-017	7075-T7351 (QQ-A-250/12)	6.350	6.250	2.250	Along 6.350 Length

RELEASED
09/07/15/W/P

B	ADDED D6101-015/-017, ADD ASTM B209	RF	09.04.23
A	NEW ISSUE	CP	01.03.30
REV.	DESCRIPTION	BY	DATE
DESIGN	CP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	RF		
CHECKED	<i>[Signature]</i>	DRAWING NO. D6101	
MFG. APPR.	<i>[Signature]</i>	REV. B SHEET 1 OF 1	
APPROVED	<i>[Signature]</i>	TITLE	
DE APPR.	<i>[Signature]</i>	SADDLE BILLET, 7075	
DATE	09.04.23	SCALE NTS	
COPYRIGHT © 2001 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO29100**

Purchase Order Date 7/10/2015

PO Print Date 7/10/2015

Page Number 1 of 2

Order From :

METAUX CASTLE
P.O. BOX 4090 STN A
TORONTO, ONTARIO M5W OE9
CANADA

VU-MET002

Ship To : DART AEROSPACE LTD

1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name

Vendor Phone

Buyer

Customer POID

Chantal Lavoie

Customer Tax #

10127-2607

Terms

Net 30

Currency

USD

FOB

Destination-Collect

Ship To Contact

Ship To Phone

Ship Via:

Yours ppd

Ship Acct:

Line Nbr	Reference Vendor Part Number Line Comments Delivery Comments	Description/ Mfg ID	Req Date/ Taxable Promise Date	CD	Req Qty/ Unit of Measure	PO Unit Price	Extended Price
1	D6101-015P	ALUM BILLET	7/27/2015 Yes 7/27/2015		20.00 Each	\$69.60	\$1,392.00

AS PER DWG D6101 REV. B
B134422

size: 9.450" X 6.250" X 2.50" thick

Tolerance on all dimensions are +0.030"/-0.000"

Grain direction along 9.450" length

Material: 7075-T7351 (QQ-A-250/12)

8/15-07-28

Line Total:

\$1,392.00

2	71401-45	PROCUREMENT QUALITY CLAUSES	7/27/2015		1.00	\$0.00	\$0.00
---	----------	--------------------------------	-----------	--	------	--------	--------

No

Procurement Quality Clauses

7/27/2015

A005 right of entry

A012 chemical and physical test report

A016 personnel qualification

A017 raw material identification (as applicable)

A026 certification of materials conformance

A041 quality management system

A042 dart notification by supplier

A043 retention of quality documents

Note:

7/10/2015

**Castle Metals®**

A. M. Castle & Co.

**PACKING SLIP/
CERTIFICATE OF CONFORMANCE**

Page 1 of 2

Shipment No:2675744

Ship From: A. M. Castle & Co. MONTREAL - CASTLE METALS 835-SELKIRK AVENUE POINTE CLAIRE, QUEBEC H9R 3S2		Sold To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CA		Ship To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CAN		Deliver To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CA	
Date Shipped 27-JUL-2015	F.O.B. ORIGIN	Freight Terms Prepaid		Carrier MANITOULIN		BOL No 2675744-2	
Shipment Details				Final Destination Branch - MON			
Order No 3975055	Line No 1	Item No 752241:MO	Description 2.5000.PL.7075.T7351.ALUMINUM.USI.48.5000.144.5000 CUT 2SIDED TO 6.25 IN (+ .0310/- .0000 IN (GRAIN TO RUN ALONG 9.45")) X 9.45 IN (+ .0310/- .0000 IN (GRAIN TO RUN ALONG 9.45")) - ALUMINUM PLATE SAW SPECIFICATIONS: AMS-QQ-A-250/12				
Purchase Order No 29100		Part Number YOUR ITEM NUMBER: D6101-015		Ordered Qty 20.00 PCS		Invoice Qty 20.00 PCS	
Details		MARK HT # ON PIECES SHIP TO CASTLE, MONTREAL (POINTE-CLAIRE) CUSTOMS BROKER: GEORGE H. YOUNG ALL PAPERWORK MUST FOLLOW ORDER / CUSTOMER MUST RECEIVE AT TIME OF DELIVERY ALL MATERIAL MUST HAVE IDENTIFYING MARKINGS EX:HEAT #'S END USER: DART AEROSPACE END USE: COMMERCIAL AIRCRAFT PARTS					
Delivery No. 120121088	Mill KAISER ALUMINUM	Heat Number 	Mech Id	PCS 20	Width (IN)	Length (IN)	Shipped Qty(LBS) 305.4241

These commodities, technology or software were exported from the United States in accordance with the Export Administration Regulations. Diversion contrary to US law prohibited.

Date Printed: 27-JUL-2015 09:50:03 AM



Castle Metals®

A. M. Castle & Co.

**PACKING SLIP/
CERTIFICATE OF CONFORMANCE**

Page 2 of 2

These commodities/technologies are subject to US Export Administration & US State Dept. Regulations and, if intended for export, were/are exported thereunder. Diversion contrary to US Law is Prohibited.	
We hereby certify the material covered by this certification conforms in accordance with the above specifications and has been found to meet the applicable requirements for the material, including any specifications forming a part of the description. Test reports are on file subject to examination. All claims for defective material are waived unless made in writing to A.M. Castle & Co. within 60 days of the shipment. Material cut to the correct size, or material cut by the customer cannot be returned for credit.	
Reviewed by Authorized Castle Metals Representative:	Date: 27 JUL 2015 Name: <i>[Signature]</i>



SHIP TO:

A M CASTLE & CO
3050 SOUTH HYDRAULIC
WICHITA, KS 67216

KAISER ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

SOLD TO:

AM CASTLE & CO- SOLD TO
1420 KENSINGTON RD
SUITE 220
OAK BROOK, IL 60523

CERTIFIED TEST REPORT

Serial Number
4376342

CUSTOMER PO NUMBER: 324790		WORK PACKAGE:		CUSTOMER PART NUMBER: 752241		SHIP RUN/LOAD: 103211/11		GOVT CONTRACT NUMBER:			
KAISER ORDER NO: 1189242		LINE ITEM: 1	SHIP DATE: 20-MAY-2015		ALLOY: 7075	CLAD: BARE	TEMPER: T7351	PRODUCT DESCRIPTION: KaiserSelect Plate			
WEIGHT SHIPPED: 3612 LB		QUANTITY: 2 PCS EST.		TRUCK B/L #: 2054006		GAUGE: 2.5000 IN (63.5000 MM)		DIAMETER/WIDTH: 48.500 IN (1231.8 MM)		LENGTH: 144.500 IN (3670.3 MM)	

MHU 1895057: LOT 13331485 2 pieces;

DAS
14
9-89

15107/29

Certified Specifications

AMS 4078/RevJ
ASTM B 209/Rev14
BSS 7055/RevB
DPS 4.713/RevAK
MMS 159/RevT

AMS-QQ-A-250/12/RevA
ASTM B 594/Rev13
CMMP 025/RevU
GAMPS 9101/RevB/AmdSCN1
PS 21211/RevM

AMS-STD-2154/RevA
BAC 5439/RevJ
CSTI 006/RevE
GSS16100/RevG/Amd1

Test Code: 4297

Test Results

Lot: 13331485 Cast 804 Drop 02 Ingot 1 Melted in USA

(ASTM E8/B557)
(EN 2002-1)

Tensile:	Temper	Dir / # Tests	Ultimate KSI (MPA)	Yield KSI (MPA)	Elongation %
	T7351	LT / 2 (Min:Max)	68.8 : 69.7 (474 : 481)	57.8 : 58.8 (399 : 405)	11.6 : 12.0

(ASTM E1004)
(EN 2004-1)

Conductivity %IACS :	40.3 Min	40.5 Max
(MS/M) :	23.4 Min	23.5 Max

(ASTM E1251)

Chemistry:	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER
Actual(wt%)	0.07	0.19	1.4	0.05	2.5	0.20	5.5	0.03	0.01	0.01	TOT 0.05



KAISER ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

CERTIFIED TEST REPORT

Serial Number
4376342

ALLOY LIMITS

	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER	MAX
7075												
MIN(wt%)	0.00	0.00	1.2	0.00	2.1	0.18	5.1	0.00	0.00	0.00	EACH	0.05
MAX(wt%)	0.40	0.50	2.0	0.30	2.9	0.28	6.1	0.20	0.05	0.05	TOT	0.15

Aluminum Remainder

ORDER COMMENTS

AMC CA-164138-R 8
AMS 4078, AMS QQ-A-250/12, AMS STD-2154, A
STM B209, ASTM B594, BS
S 7055, CMMP-025, CSTI 006, DPS 4.713, GAMP
S 9101, MMS 159, PS 212

11

DAS
14
9-89

1507/29

TEST NOTES

Metal represented by this test report was 100% immersion ultrasonically tested from one side with 3mm dead zones top and bottom and meets the Class A and Class B requirements of all specifications referenced on this test report. No surface marking or sonic indications is performed.

CERTIFICATION

Kaiser Aluminum Fabricated Products, LLC (Kaiser), is ISO-9001:2008/AS9100C certified and hereby certifies that all material shipped under this order:

- has been inspected, tested, and found to be in conformance with the requirements of the specifications indicated herein. For material thicknesses outside specification limits, mechanical properties are as shown herein and chemical composition meets specification requirements.
- was melted in the United States of America or a qualifying country per DFARS 225.872-1(e), was manufactured in the United States of America, and meets the requirements of DFARS 252.225 (a) domestic content.
- has been thermally processed in compliance with AMS 2772, where applicable;
- is mercury free, within the limits of detection of ASTM E1231 (≤ 1 ppm);
- is in compliance with RoHS 2, European Union Directives 2011/65/EU;
- is in compliance with and regularly monitors any updates to the European Chemical Agency, ECHA, REACH regulations, (EC) n°1907/2006;
- is free of Conflict Minerals, as defined in Section 15.2 of the Dodd-Frank Act.

Any warranty is limited to that shown on Kaiser Aluminum's standard general terms and conditions of sale. Test reports are on file, subject to examination. Test reports shall not be reproduced except in full, without the written approval of the Kaiser Aluminum laboratory. The recording of false, fictitious or fraudulent statements or entries on the certificate may be punished as a felony under federal law.

James Hemenway

JAMES HEMENWAY, LABORATORIES SUPERVISOR

Page 2 of 2



MATERIAL RECEIPT INSPECTION FORM

MATERIAL: D6101-015
 DATE: 15/07/29

PO / BATCH NO: 29100 / B134422

MATERIAL CERT REC'D: yes
 QUANTITY RECEIVED: 20
 QUANTITY INSPECTED: 20
 QUANTITY REJECTED: _____

THICKNESS ORDERED: 9.40X6.25X2.50
 THICKNESS RECEIVED: 9.40X6.25X2.50
 SHEET SIZE ORDERED: _____
 SHEET SIZE RECEIVED: _____

DESCRIPTION	NCR (Check Y/N)	COMMENTS
SURFACE DAMAGE	Y ☒ N ☐	
CORRECT FINISH	☒ Y ☐ N ☐	
CORROSION	Y ☐ N ☒	
CORRECT GRAIN DIRECTION	☒ Y ☐ N ☐	
CORRECT MATERIAL	☒ Y ☐ N ☐	
CORRECT THICKNESS	☒ Y ☐ N ☐	
PHOTO REQUIRED	Y ☐ N ☒	
CORRECT MATERIAL	☒ Y ☐ N ☐	
CORRECT REF # TO LINK CERT	☒ Y ☐ N ☐	
CORRECT MATERIAL IDENTIFICATION	☒ Y ☐ N ☐	
CORRECT M# ON THE MATERIAL	☒ Y ☐ N ☐	
DOES THIS MATERIAL REQUIRE ENGINEERING SIGN OFF	Y ☐ N ☒	
DOES THIS REQUIRE AN EXTRUSION REPORT	Y ☐ N ☒	

CUT SAMPLE PIECE OF MATERIAL AND PREFORM A HARDNESS CHECK. RECORD RESULTS BELOW				
TYPE OF MATERIAL	HRC	HRB	DUR A	DUR D
SIZE OF TEST SAMPLE				
HARDNESS / DUROMETER READING				

testers located in the Quality Office

QC 18 INSPECTION	ENGINEERING SIGNOFF (if required)
INSPECTED BY: <u>DAS</u> <u>14</u> DATE: <u>15/07/29</u>	SIGNED OFF BY: _____ DATE: _____

Attach this inspection sheet with the corresponding material cert and remit to be scanned and received in

MATERIAL RECEIPT INSPECTION FORM

INSTRUCTIONS FOR INSPECTING BAR, TUBING, ROUND, & SHEET STOCK

- 1- VERIFY STOCK TO DART PURCHASE ORDER
- 2- MEASURE ALL DIMENSIONS FOR EACH PURCHASED STOCK
 - a. WIDTH, THICKNESS, DIAMETER, WALL THICKNESS & LENGTH
- 3- VERIFY CONDITION OF MATERIAL i.e. DAMAGED, CORRODED, etc.
- 4- VERIFY THAT SUPPLIER HAS A NUMBER (HEAT #) ON ITS RECEIVING REPORT TO LINK TO MATERIAL CERTS
- 5- VERIFY MATERIAL CERTS ARE CORRECT TO THE DART PO INSTRUCTIONS
- 6- REMOVE / CUT A PIECE OF MATERIAL FOR SAMPLE HARDNESS TESTING

INSTRUCTIONS FOR INSPECTING SKIDTUBE & STEP EXTRUSION

- 1- VERIFY TO DART SUPPLIED DRAWING
- 2- SAMPLE INSPECT MATERIAL IN BUNDLE TO ENSURE MATERIAL CAN BE RECEIVED INTO DART
- 3- USING PORTABLE HARDNESS TESTER VERIFY HARDNESS OF THE MATERIAL TO THE DRAWING
- 4- VERIFY THAT MATERIAL CERTS MATCH TO WHATS CALLED UP ON THE DART DRAWING

AFTER MATERIAL PASSES INSPECTION

- 5- HAVE DART EMPLOYEES START STOCKING MATERIAL BUT REQUEST MIN 20pcs FOR FULL INSPECTION
- 6- INSPECT ALL DIMS AS PER DRAWING REQUIREMENTS

INSTRUCTIONS FOR INSPECTING CROSS TUBE MATERIAL

- 1- VERIFY MATERIAL CERTS MATCH THE REQUIREMENTS ON THE DART DRAWINGS
- 2- INSPECT MIN. HALF THE BATCH OF EXTRUSION RECEIVED INTO DART
- 3- INSPECT MATERIAL AS PER THE EXTRUSION REPORT
 - a. WALL THICKNESS USING ULTRA-SONIC IN 4 LOCATIONS
 - b. OUTSIDE DIAMETER HIGHEST/LOWEST BOTH ENDS
 - c. INSIDE DIAMETER HIGHEST/LOWEST BOTH ENDS
 - d. STRAIGHTNESS @ CENTER OVER 12" SPAN
 - e. WALL THICKNESS USING TUBE MICROMETER HIGHEST/LOWEST BOTH ENDS
- 4- IDENTIFY EACH TUBE IN SEQUENCE OF INSPECTING (TUBE 1, TUBE2.....) AND W/O# AND PO#
- 5- RECORD ALL FINDINGS ON EXTRUSION REPORT

IF ANY QUESTIONS PLEASE SEE QC COORDINATOR BEFORE GOING FURTHER
